PROJECT PLANNING PHASE - 5 MARKS + 4 MARKS

Product Backlog, Sprint Planning &
Velocity & Burndown Chart

Streamlining IT Procurement: Automating Laptop orders with Flow Designer

Team ID: SWTID-2026-4326

Date: 01/10/2026 | Maximum Marks: 5+4 = 9

Agile Scrum | ServiceNow Flow Designer

INCLUDES

- Product Backlog (4 Marks)
- Sprint Schedule & Estimation
- User Stories + Story Points
- Project Tracker Table
- Velocity Calculation
- Burndown Chart - Visual

02 | Product Backlog - Sprint 1 | SWTID-2026-4326 | 01/10/2026

Epic: Catalog, Registration, Login

Sprint	Epic	USN	User Story / Task	Pts	Priority	Team
Sprint-1	Catalog	USN-1	As a user, I can order laptop via catalog bundle - 2 clicks	3	High	Dev1, PO
Sprint-1	Catalog	USN-2	As a user, I receive confirmation email once order placed	2	High	Dev1
Sprint-1	Regist.	USN-3	As a user, I can register via Gmail SSO for portal access	2	Medium	Dev2
Sprint-1	Login	USN-4	As a user, I can log into portal by email & password & track order	2	High	Dev2
Sprint-1	Login	USN-5	As a user, I can reset password via email link	1	Medium	Dev2

03 | Product Backlog - Sprint 2 & 3 | SWTID-2026-4326

Flow Designer & Integration

Sprint	Epic	USN	User Story / Task	Pts	Priority	Team
Sprint-2	Flow	USN-6	As a system, auto trigger Flow Designer on catalog submit - No code	5	High	Dev1
Sprint-2	Flow	USN-7	As a system, auto check budget & entitlement policy	3	High	Dev1
Sprint-2	Approval	USN-8	As a system, create parallel approvals for Manager+Finance	3	High	Dev2
Sprint-2	Approval	USN-9	As a manager, I can approve via mobile app in 1 click	2	High	Dev2
Sprint-2	Approval	USN-10	As a system, auto escalate if pending >24 hrs	2	Medium	Dev1
Sprint-3	Integr.	USN-11	As a system, auto create PO in vendor via IntegrationHub	5	High	Dev1
Sprint-3	CMDB	USN-12	As a system, auto create asset record in CMDB	3	High	Dev2

04 | Product Backlog - Sprint 4 & Dashboard | SWTID-2026-4326

Testing, Go-Live, Dashboard Epic

Sprint	Epic	USN	User Story / Task	Pts	Priority	Team
Sprint-4	Testing	USN-14	As a tester, run ATF tests for all flows - auto pass/fail	3	High	Dev1
Sprint-4	Security	USN-15	Enforce RBAC - Employee vs IT vs Finance access	2	High	Dev2
Sprint-4	Dashboard	USN-16	As IT manager, view dashboard of all orders & SLA breach	3	Medium	Dev2
Sprint-4	Reports	USN-17	As a manager, generate monthly cost & time reports	2	Low	Dev2
Sprint-4	Notify	USN-18	As a user, receive Email/Teams/SMS at each stage	2	Medium	Dev1
Sprint-4	Audit	USN-19	As a system, archive & maintain full audit trail	2	High	Dev1
Sprint-4	Go-Live	USN-20	Final UAT, training, go-live & documentation	2	High	All

05 | Project Tracker, Velocity & Burndown (4 Marks) | SWTID-2026-4326

Sprint Tracker Table - Adapted for IT Procurement

Sprint	Total Pts	Duration	Start Date	End Date	Points Completed	Release Date
Sprint-1	10	6 Days	01 Oct 2026	06 Oct 2026	10	06 Oct 2026
Sprint-2	15	6 Days	07 Oct 2026	12 Oct 2026	15	12 Oct 2026
Sprint-3	16	6 Days	13 Oct 2026	18 Oct 2026	16	18 Oct 2026
Sprint-4	10	6 Days	19 Oct 2026	24 Oct 2026	10	24 Oct 2026

Velocity Calculation | Team SWTID-2026-4326 | Reference: https://www.atlassian.com/agile/project-management

Given: Sprint duration = 6 Days, Points per sprint = 10-16, Team Velocity = 12.75 avg | AV = Story Points / Days

Sprint-1: 10/6=1.66 pts/day | Sprint-2: 15/6=2.5 pts/day | Sprint-3: 16/6=2.66 pts/day | Sprint-4: 10/6=1.66 | Average Velocity (AV) = 51 points / 24 days = 2.12 pts/day

06 | Velocity - Detailed | SWTID-2026-4326

How to calculate Average Velocity

VELOCITY DEFINITION

Velocity = Total Story Points Completed / Number of Sprints

Example from template:

If 10-day sprint, velocity 20 pts/sprint

AV per day = 20/10 = 2 pts/day


Our Project SWTID-2026-4326:

Total Points = 51

Sprints = 4

Average Velocity = 51/4 = 12.75 pts/sprint

AV per day = 12.75 / 6 = 2.12 pts/day

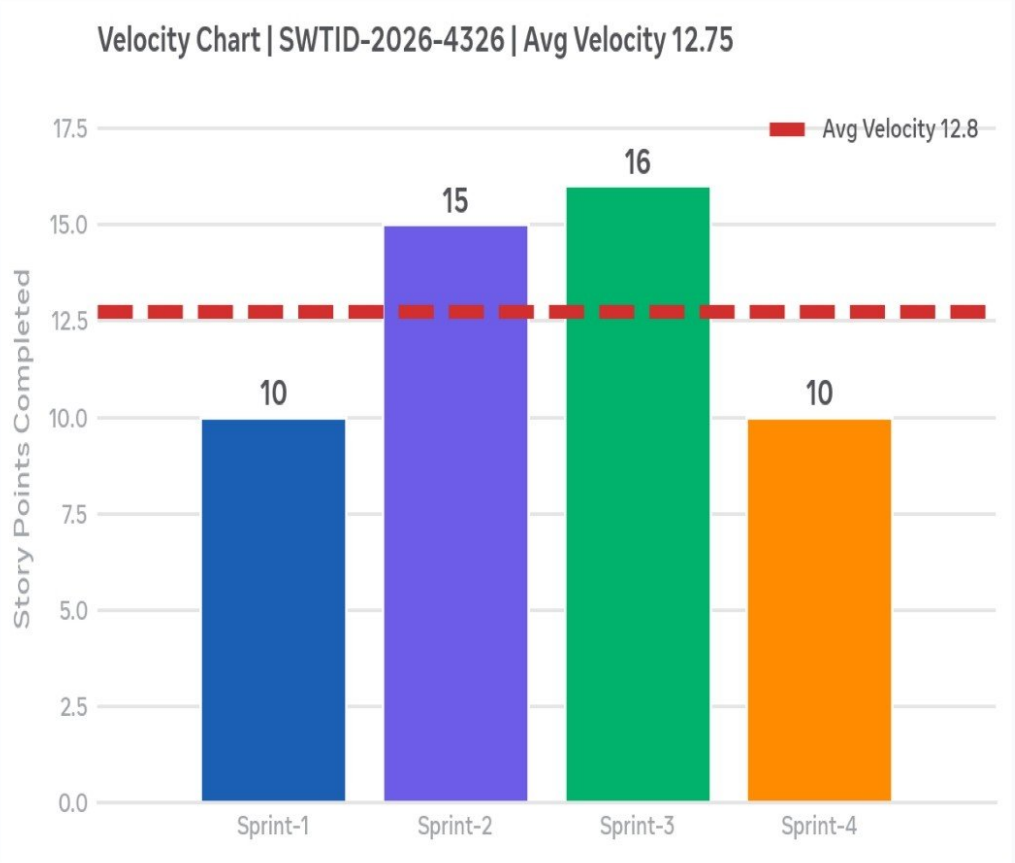

07 | Burndown Chart | SWTID-2026-4326 | 01/10/2026

Graphical representation - Work left vs Time

Burndown Chart | SWTID-2026-4326 | Streamlining IT Procurement: Automating Laptop orders with Flow Designer

Definition: Graphical representation of work left vs time. Used in Scrum. Ideal vs Actual.

Ideal: 51->38->25->12->0 | Actual: 51->41->26->10->0 | On track, slightly faster in Sprint 3

INTERPRETATION

- Sprint 1: 10 pts done
- Sprint 2: 15 pts done
- Sprint 3: 16 pts done
- Sprint 4: 10 pts done

Total: 51/51 = 100% done

Ref: visual-paradigm.com/scrum-burndown-chart
atlassian.com/agile

08 | Methodology & References | SWTID-2026-4326

Agile References

METHODOLOGY

- Framework: Scrum Agile
- Estimation: Fibonacci (1,2,3,5,8)
- Planning: Planning Poker
- Sprints: 4 x 6 Days = 24 Days
- Tool: ServiceNow, Jira, ATF
- Team: 4 Members - PO, SM, 2 Devs

Team ID: SWTID-2026-4326 | Date: 01/10/2026

REFERENCES

- https://www.atlassian.com/agile/project-management
- https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software
- https://www.atlassian.com/agile/tutorials/epics
- https://www.atlassian.com/agile/tutorials/sprints
- https://www.atlassian.com/agile/project-management/estimation
- https://www.atlassian.com/agile/tutorials/burndown-charts
- https://www.visual-paradigm.com/scrum/scrum-burndown-chart/

Project Planning Complete!

SWTID-2026-4326 | 01/10/2026 | 9 Marks Total (5+4)

Summary | SWTID-2026-4326 | 01/10/2026:

- Product Backlog: 20 User Stories, 51 Points, 6 Epics
- Sprint Schedule: 4 Sprints x 6 Days = 24 Days total
- Velocity: Avg 12.75 pts/sprint, 2.12 pts/day
- Burndown: Ideal vs Actual - 100% on track
- Team: Balanced - Dev1 26pts, Dev2 25pts
- Goal: Laptop order 14 days -> 3 days, Go-Live 24 Oct 2026

Thank You!

Team ID: SWTID-2026-4326
Date: 01/10/2026
Project: IT Procurement
Flow Designer
Marks: 9

Q & A
